


SR 347 Schedule Update





Ames Construction

- Chris Kane – Project Manager
- Nick DeVito – Project Superintendent


ADOT

- Micah Hanam – Resident Engineer
- Denver Romaine – Superintendent

City of Maricopa

- Bill Fay
- Wes Carnahan



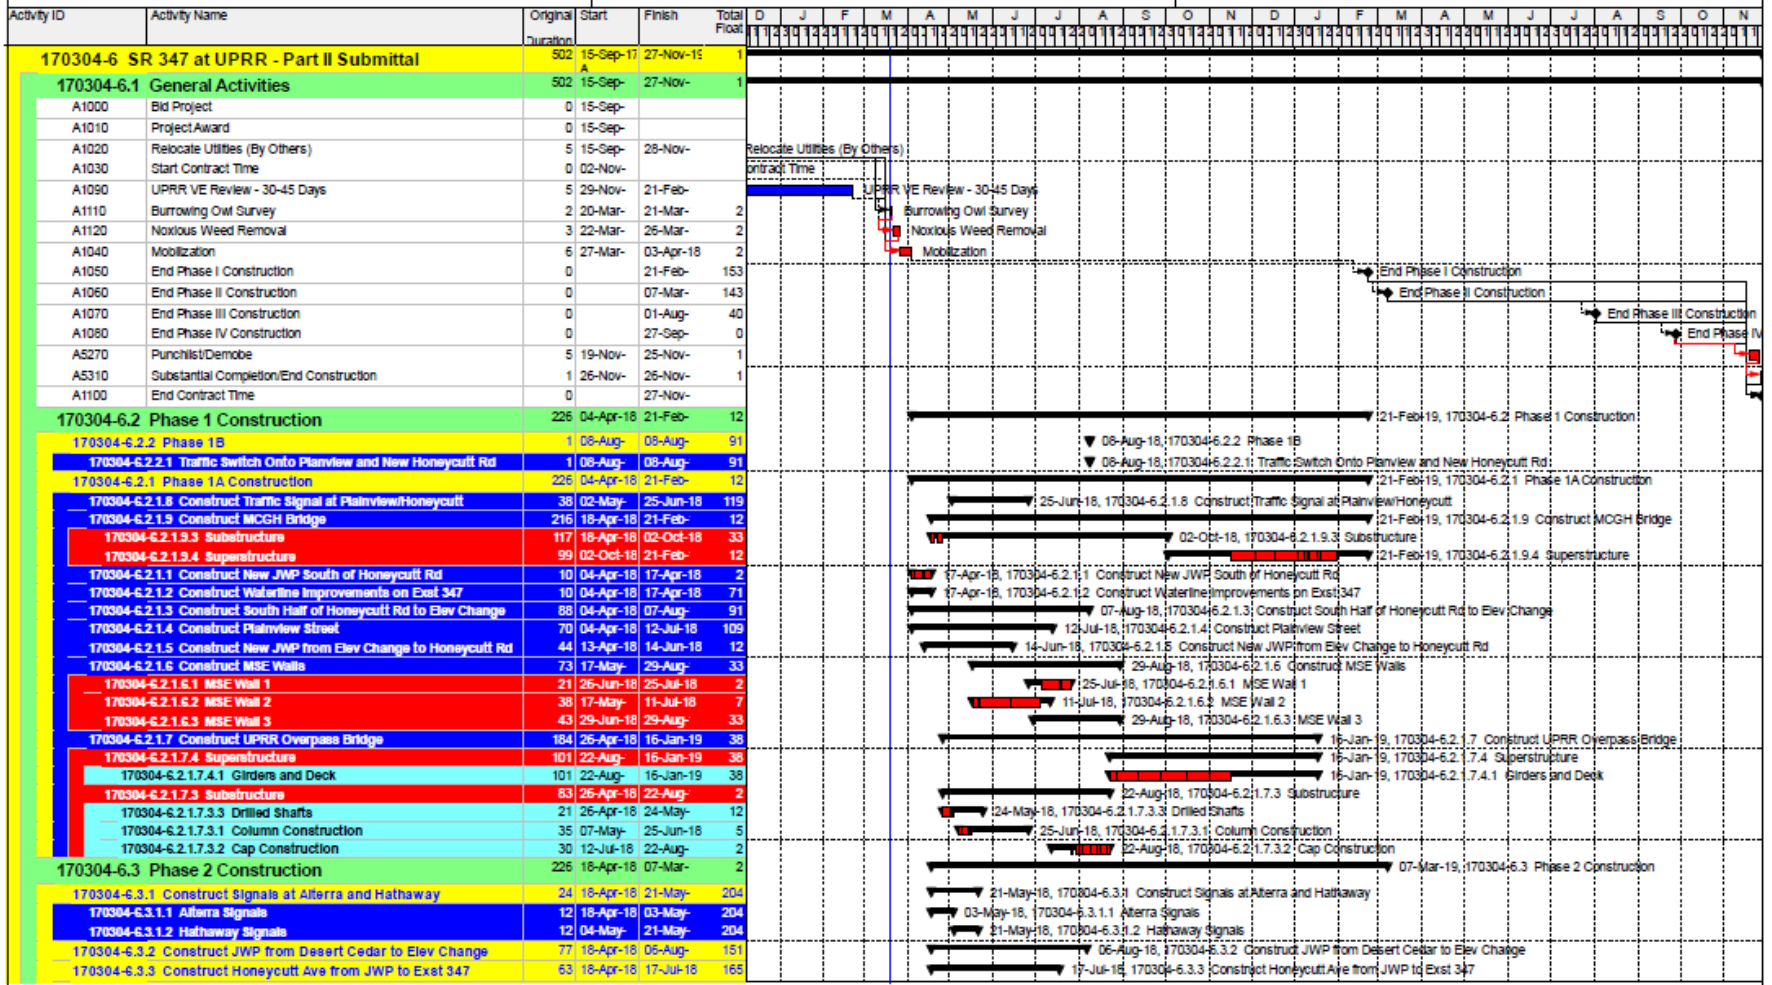

█ Remaining Level of Effort
 █ Remaining Work
 █ Actual Work
 █ Critical Remaining Work
 ◆ Milestone
 ◀ Summary



Key Dates

- End Phase I Construction 21-Feb-19
- End Phase II Construction 07-Mar-19
- End Phase III Construction 01-Aug-19
- End Phase IV Construction 27-Sep-19
- Punchlist/Demobe 19-Nov-19 to 25-Nov-19
- Substantial Completion/End Construction
26-Nov-19
- End Contract Time 27-Nov-19



Acknowledgements

Construct Traffic Signal at Plainview/Honeycutt 02-May-18 to 25-Jun-18

Construct UPRR Overpass Bridge 26-Apr-18 to 16-Jan-19
Superstructure 22-Aug-18 16-Jan-19

Construct Waterline Improvements on Exst 347 04-Apr-18 to 17-Apr-18

Construct North Half of Honeycutt to JWP 09-Aug-18 to 07-Mar-19 2

Construct New JWP from Honeycutt Rd to Exst 18-Apr-18 to 15-Feb-19 16

New JWP from Elevation Break North to UPRR (Phase 1) 26-Jul-18 to 21-Nov-18



Questions or Comments?

